


# Major transport infrastructure timeframes (March 2026)

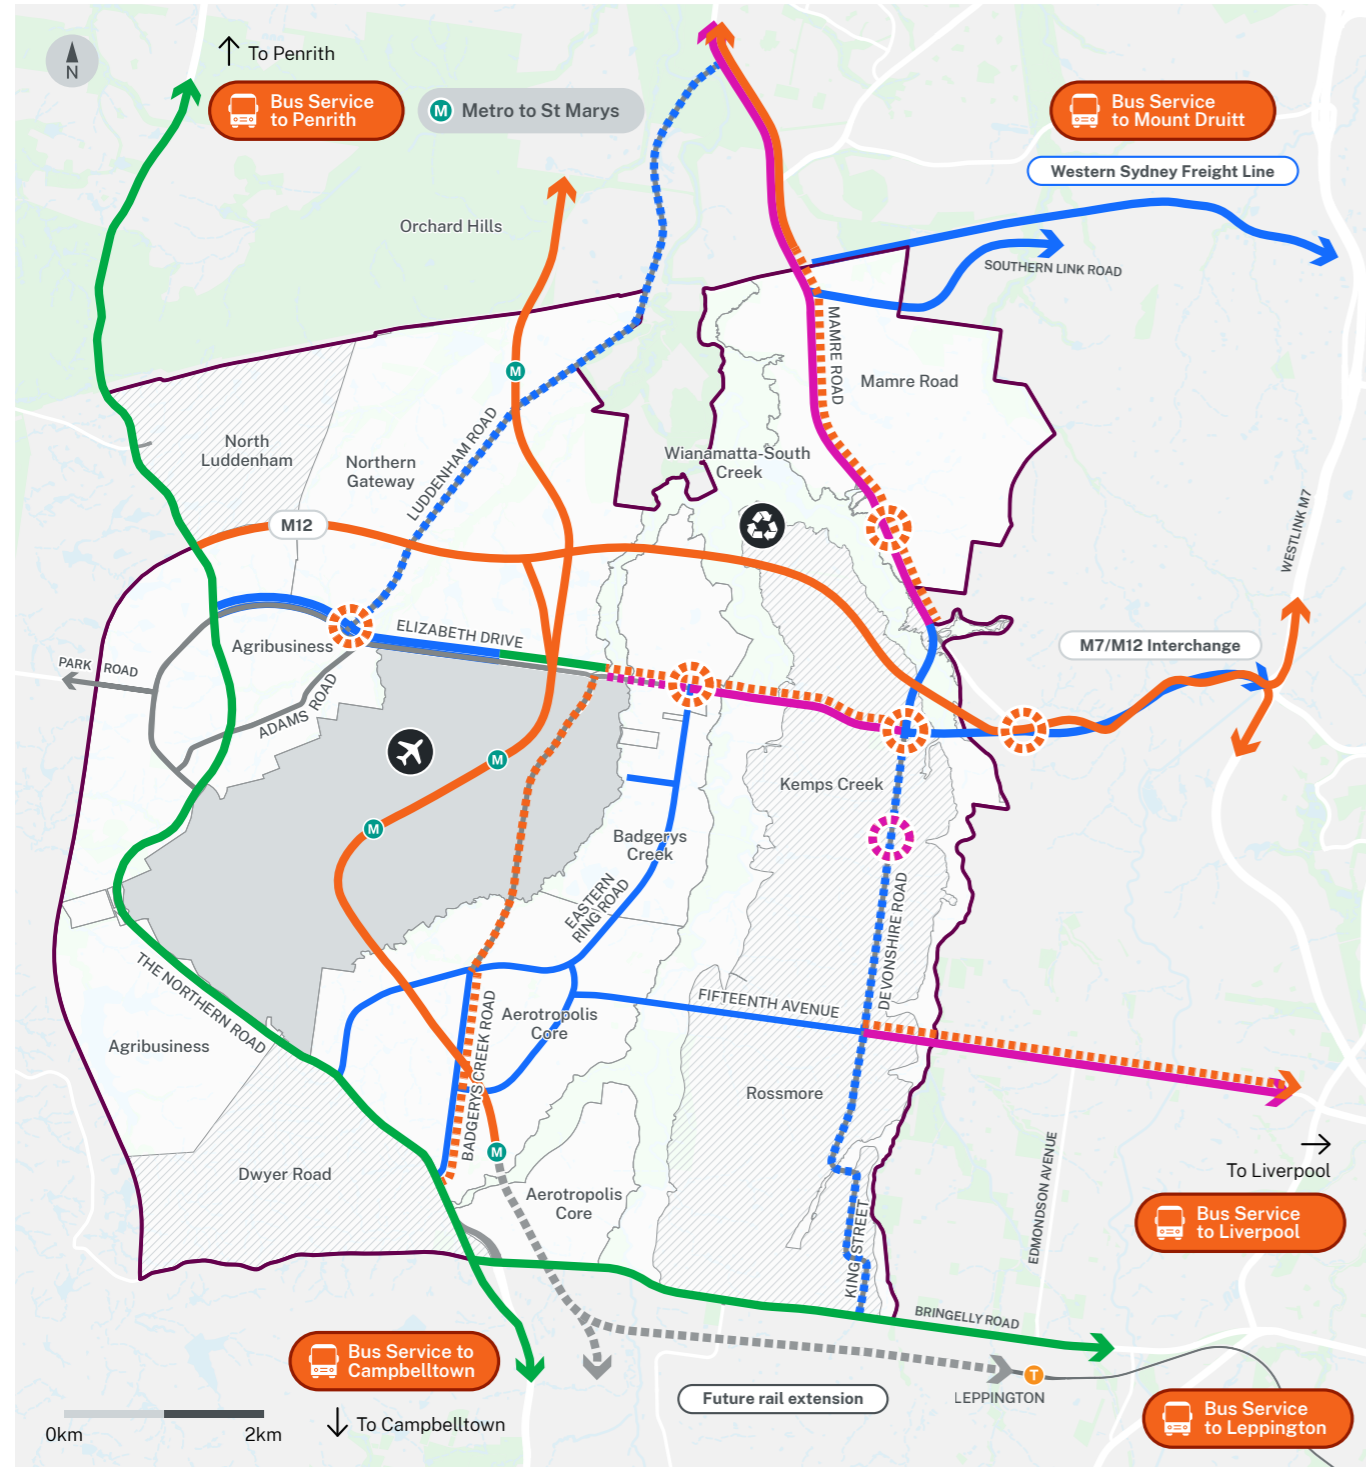

**LEGEND**

- Aerotropolis boundary
- Precinct boundaries
- Future rezonings
- Sydney Metro station
- Western Sydney International Airport
- Advanced Water Recycling Centre

**DEVELOPMENT STATUS**

- Existing infrastructure
- Future rail extension
- Recently completed/major upgrades

**EARLY AIRPORT OPERATIONS (2027)**

- Works in progress/delivered
- Safety works/interim upgrades
- Intersection upgrades

**2030 PRIORITIES**

- Works in progress/delivered
- Safety works/interim upgrades
- Intersection upgrades

**2040 PRIORITIES**

- Works in progress/delivered
- Safety works/interim upgrades

## Key enabling infrastructure to service the Aerotropolis

Project	2027	2030	2040	Status
<b>Major road infrastructure</b>				
<b>Badgerys Creek Road (Corridor) Interim safety upgrade</b>	▨			Works underway including line marking and resurfacing, due for completion by mid-2026.
<b>Badgerys Creek Road South* Planned major upgrade</b>	XX	XX		Full Business Case (FBC) being prepared, due for completion in 2027 (The Northern Road to Eastern Ring Road).
<b>Bradfield Metro Link Road* Planned new road</b>	XX	XX		Funding provided for FBC in 2025-26 NSW Budget and as part of Australian Government election announcement.
<b>Devonshire Road* Planned major upgrade</b>	XX	XX		Funding provided for FBC in 2025-26 NSW Budget.
<b>Devonshire Link Road* Planned new road</b>	XX	XX		Funding provided for FBC in 2025-26 NSW Budget and as part of Australian Government election announcement. FBC due for completion in 2027.
<b>Eastern Ring Road* Planned new road</b>	XX	XX		FBC being prepared, due for completion in 2027.
<b>Elizabeth Drive East (Devonshire Road towards Badgerys Creek Road) Major upgrade</b>		✓		Land acquisition and on-site investigations are underway. Construction tenders invited in December 2025. Early works due to commence in Q4-2026.
<b>Elizabeth Drive East (Devonshire Road to M7)* Planned major upgrade</b>	▨			New on-ramps from Elizabeth Drive will allow toll-free access to the new M12 motorway by early-2026.
<b>Elizabeth Drive West* Planned major upgrade</b>	▨			Upgrade to 2.2km of Elizabeth Drive at WSI Airport access point completed. This includes tie-in works with remaining roadway.
<b>Fifteenth Avenue* Major upgrade / planned new road</b>			✓	Devonshire Road to Cowpasture Road prioritised for Stage 1 delivery. Early safety works and intersection upgrades are in progress.
<b>Luddenham Road* Planned major upgrade</b>	▨		XX	Funding provided for signalisation of Elizabeth Drive intersection in 2025-26 NSW Budget.
<b>Mamre Road Stage 1 Major upgrade</b>		✓		Major construction commenced in 2024 (between M4 Motorway and Erskine Park Road). Due for completion in 2028.
<b>Mamre Road Stage 2 Major upgrade</b>		✓		REF submissions closed in Nov 2025 (Erskine Park Road to Kerrs Road). Construction tender invited in Dec 2025. Works due to commence in late 2026.
<b>M12 Motorway / M7-M12 Integration New motorway and upgrade</b>	✓			New M12 motorway due to open to traffic in early 2026. Works underway for M7 widening and M7/M12 interchange. Completion expected in 2026.
<b>Pitt Street West* Planned major upgrade</b>	XX	XX		No update.
<b>Southern Link Road Stage 1* Planned major upgrade/new road</b>	XX	XX		FBC (Mamre Road to Compass Drive) expected to be completed in 2026.
<b>Rail and bus services</b>				
<b>Western Sydney Bus Services Phase 1</b>		✓		Services between WSI Airport and Bradfield to major centres will commence in mid-2026. Free interim bus services between WSI Airport and St Marys will commence upon the start of passenger operations, prior to the commencement of Metro services.
<b>Western Sydney Bus Services Phase 2*</b>			✓	No update.
<b>Western Sydney Rail Extensions*</b>	XX	XX		FBCs being prepared for rail extensions from Bradfield to Leppington and Campbelltown; and St Marys to Tallawong, due in 2026. These will inform a government decision on sequencing and timing of delivery. \$1 billion committed by Australian Government towards southern corridor land acquisition.
<b>Sydney Metro – WSI Airport</b>		✓		Major construction underway.
<b>Western Sydney Freight Line and Intermodal Terminal (Stage 1)*</b>	XX	XX		FBC due for completion in 2026.
<b>Major wastewater infrastructure (in delivery)</b>				
<b>Upper South Creek Advanced Water Recycling Centre</b>	✓			Major construction underway, due for completion in 2026.
<b>Stage 1: Wastewater Network</b>	✓			Construction underway to enable servicing of Mamre Road, Badgerys Creek, Northern Gateway, and parts of Agribusiness and Aerotropolis Core precincts.
<b>Stage 2: Wastewater Network</b>		✓		Construction underway to enable servicing of remaining Agribusiness and Aerotropolis Core areas.

\* Identified as a priority for future delivery subject to funding

**Legend** ▨ Interim safety upgrades    XX Full business case complete    Construction    ✓ Project complete
